

Northern Line Extension

PROGRESS UPDATE

December 2019-February 2020

NLE Kennington Green

Thank you for your patience whilst we continue with the Northern Line Extension (NLE) works near you. We would like to update you on where we are and what is planned over the coming months.

What has been completed?

The utility works on Montford Place for our electricity supply for the headhouse have been completed and the road has been reinstated.

Within the basement of the Kennington Green site, the fit out and mechanical and electrical works are progressing well. A lot of equipment is now being installed and power is now live – this is a major milestone for the overall completion of the Northern Line Extension.

At the surface we have commenced with the waterproofing membrane installation over the top of the basement – this will continue in January and February.



Fig. 1 Overview of Kennington Green site

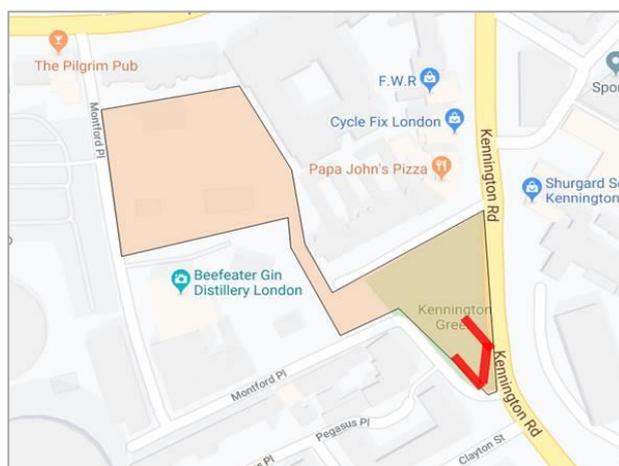


Fig.2 Red highlighted section of break out works

What is planned?

Specialist contractors are now on board and will continue with the 'fit out' works including installation of mechanical and electrical equipment. The installation of the brickwork façade of the head house is now due to commence in January.

This week (w/c 16/12), we will be removing part of the foundation around the shaft (see Fig. 2 above), which was installed to support the acoustic shed that was in place during the tunnelling works. This will involve an excavator working to break out the concrete and load it onto transport for removal from site. Works will take place between core working hours only.

Preparation for landscaping works will commence towards the end of February. An updated notice will be issued nearer the time to advise of the arrangements for properties around the Green and Montford Place. The site will close for the Christmas period mid-afternoon on the 24 December and we will return on the 02 January 2020.

nle@tfl.gov.uk

0343 222 2424 (option 1)

tfl.gov.uk/northern-line-extension
